

Job #:

Ref #:

Date: Friday 17th July 15

Customer /Client: R. Osprey

Site Address: Deane Park phase 2.

1. Plant Used:

320 D Cat excavator + Rock wheel

210 Komatsu excavator + Rock teeth buckets/chains/slags

16t Hyundai excavator + Trench wacker + buckets

Cab CB 24 Roller

6t dumper

Trench box 1.5m x 4m x 2m deep

3m x 3m x 2m deep.

2. Labour Used:

Foreman - Simon Jackson

Laborer/ops - X3

Elite Groundworks & Construction Contractors Ltd

Daily Job/Contract Variation Sheet

Job #:

Ref #:

Date:

Customer /Client:

Site Address:

3. Materials Used:

4. Consumable Items Used:

5. Collection of Materials:

6. Further information on Works Undertaken:

Laying of 525 ϕ between 56-54 / track reinstated.
Laying / compaction of 225mm T/P 1 met between 59-510.

Elite Groundworks & Construction Contractors Ltd

Daily Job/Contract Variation Sheet

Job #:

Ref #:


Date:

Customer /Client:

Site Address:

To be completed by operatives carrying out the work and the Main Contractor / Client /Customer.

For and on behalf of Elite Groundworks & Construction Contractors Ltd:

<u>Name (Print):</u>	<u>Signature:</u>	<u>Date:</u>
X S Jackson	X 	X 17/7/15
X P Wellings	X	X 17/7/15
X W Ridge way.	X	X 17/7/15
X A Clenson	X	X 17/7/15

For Main Contractor/Client

<u>Name (Print):</u>	<u>Signature:</u>	<u>Date:</u>
X	X	X
X	X	X
X	X	X
X	X	X

Elite Groundworks & Construction Contractors Ltd

Daily Job/Contract Variation Sheet

Job #:


Ref #:

Date:

Customer /Client:

Site Address:

6. Office Use Only:

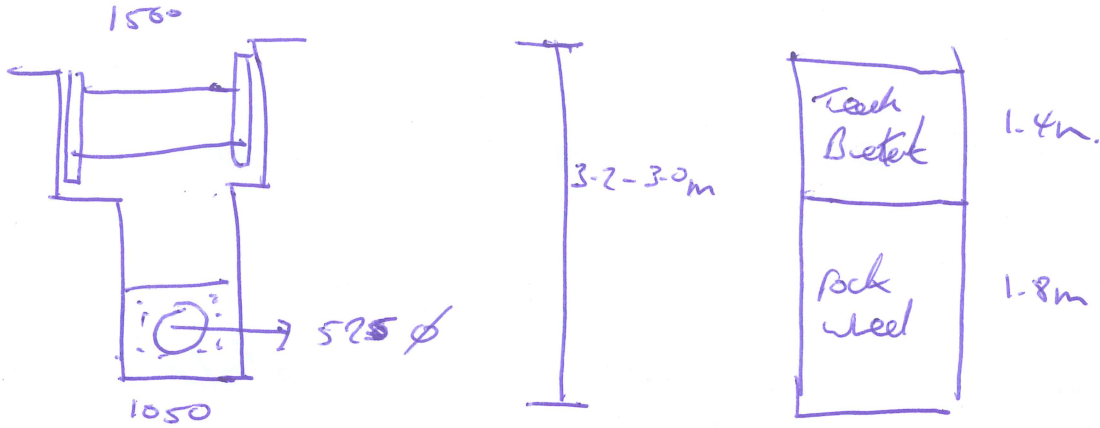

525 ϕ x 2.5m @ n°

Backfill - 10-50 x 1050mm Treedweller
1400 x 1500mm Roller

Hardcore - level/grade 1/2" not hardcore with
Hydramat excavator/compacted cat core roller.
8-3m wide @ 225mm deep
S9 - S10.
