

Daily Job/Contract Variation Sheet

Job #: _____ Ref #: _____ Date: 7/July/15
Customer /Client: K. O'Spally's.
Site Address: Deven Park - phase 2.

1. Plant Used:

21 + Komatsu + Rock teeth.
20t Cat + Rock wheel
16t Hyundai + trench winker.
Trench box + manhole shutter
6t dumper
120 roller.

2. Labour Used:

Fore man - 5-man Snelson
Labour - X3.

Elite Groundworks & Construction Contractors Ltd

Daily Job/Contract Variation Sheet

Job #: _____ Ref #: _____ Date: _____

Customer /Client: _____

Site Address: _____

3. Materials Used:

--

4. Consumable Items Used:

190 lts Road diesel.
7 x Rock teeth.

5. Collection of Materials:

--

6. Further information on Works Undertaken:

--

Elite Groundworks & Construction Contractors Ltd

Daily Job/Contract Variation Sheet


Job #: _____ Ref #: _____ Date: _____

Customer /Client: _____

Site Address: _____

To be completed by operatives carrying out the work and the Main Contractor / Client /Customer.

For and on behalf of Elite Groundworks & Construction Contractors Ltd:

<u>Name (Print):</u>	<u>Signature:</u>	<u>Date:</u>
X S Jackson.	X 	X 7/July/15.
X A Clenson	X	X
X P Welling	X	X
X W Ridge way	X	X

For Main Contractor/Client

<u>Name (Print):</u>	<u>Signature:</u>	<u>Date:</u>
X	X	X
X	X	X
X	X	X
X	X	X

Elite Groundworks & Construction Contractors Ltd

Daily Job/Contract Variation Sheet


Job #: _____ Ref #: _____ Date: _____

Customer /Client: _____

Site Address: _____

6. Office Use Only:

S10 - 59 150 \varnothing pipe work + Y Junctions.
4m - 3m deep. x 204m

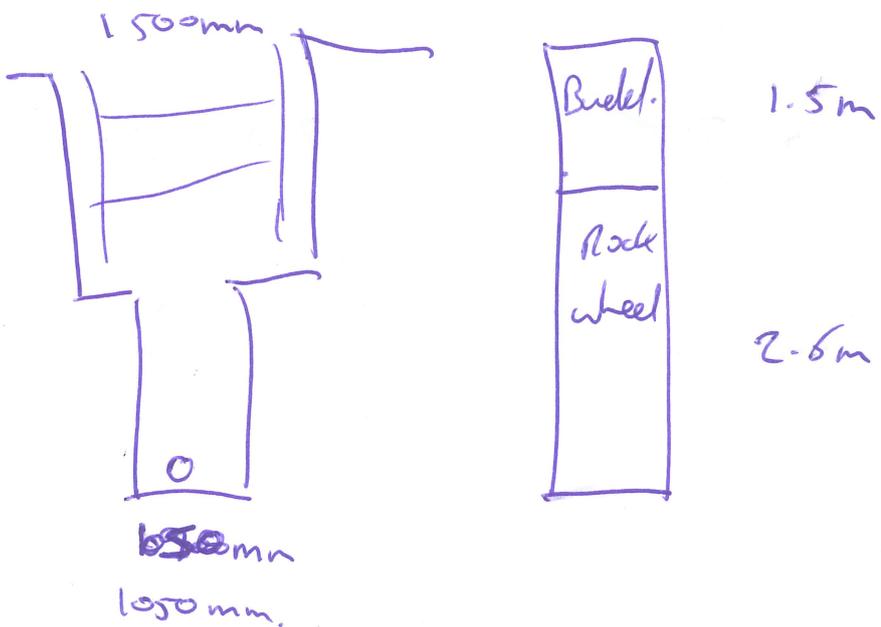

+ Backfill 1/2 way.

2 x Y Junctions,
1 x Rocker pipe.
